



June 20, 2001 Construction Committee

Contract C0326

101 Freeway Overcrossing Rendering



Contract C0326

Universal City


101 Freeway Overcrossing




- Mechanically Stabilized Earth (MSE) Wall on Caltrans Right-of-Way 100% complete.
- MSE Wall on LA City Right-of-Way on hold, 0% complete.
- 70% of all MSE Walls lie on LA City Right-of-Way.

Contract C2327

L.A. River Bridge Widening

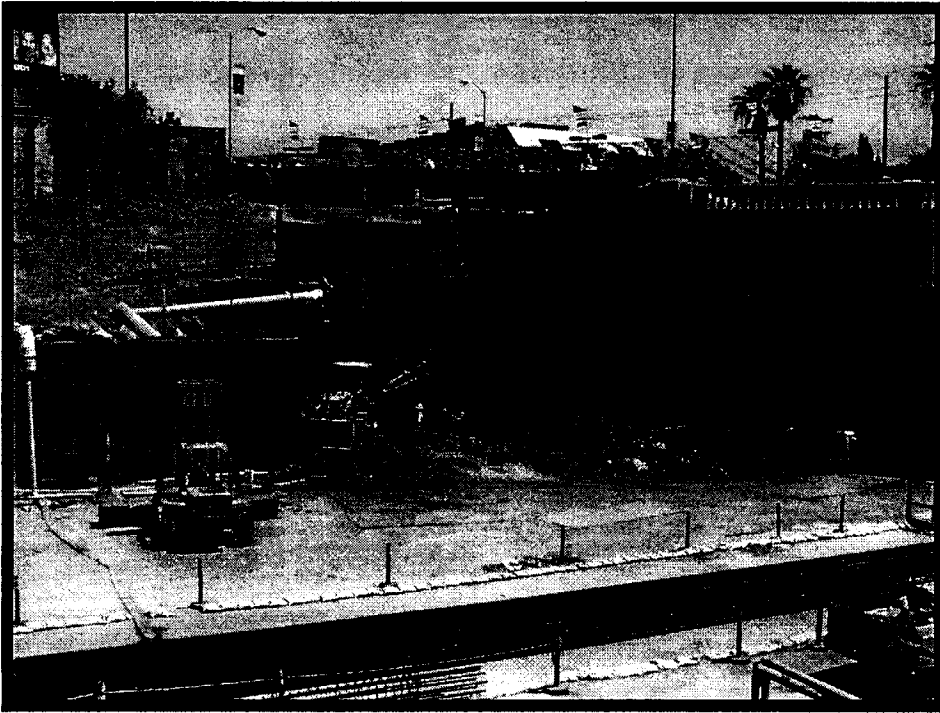

- **74% of all Cast In-place Drilled Hole (CIDH) piles have been installed for both abutments.**
 - **100% have been installed on south side abutment.**
 - **58% have been installed on north side abutment.**
- **Continuing excavation for future abutment foundations.**

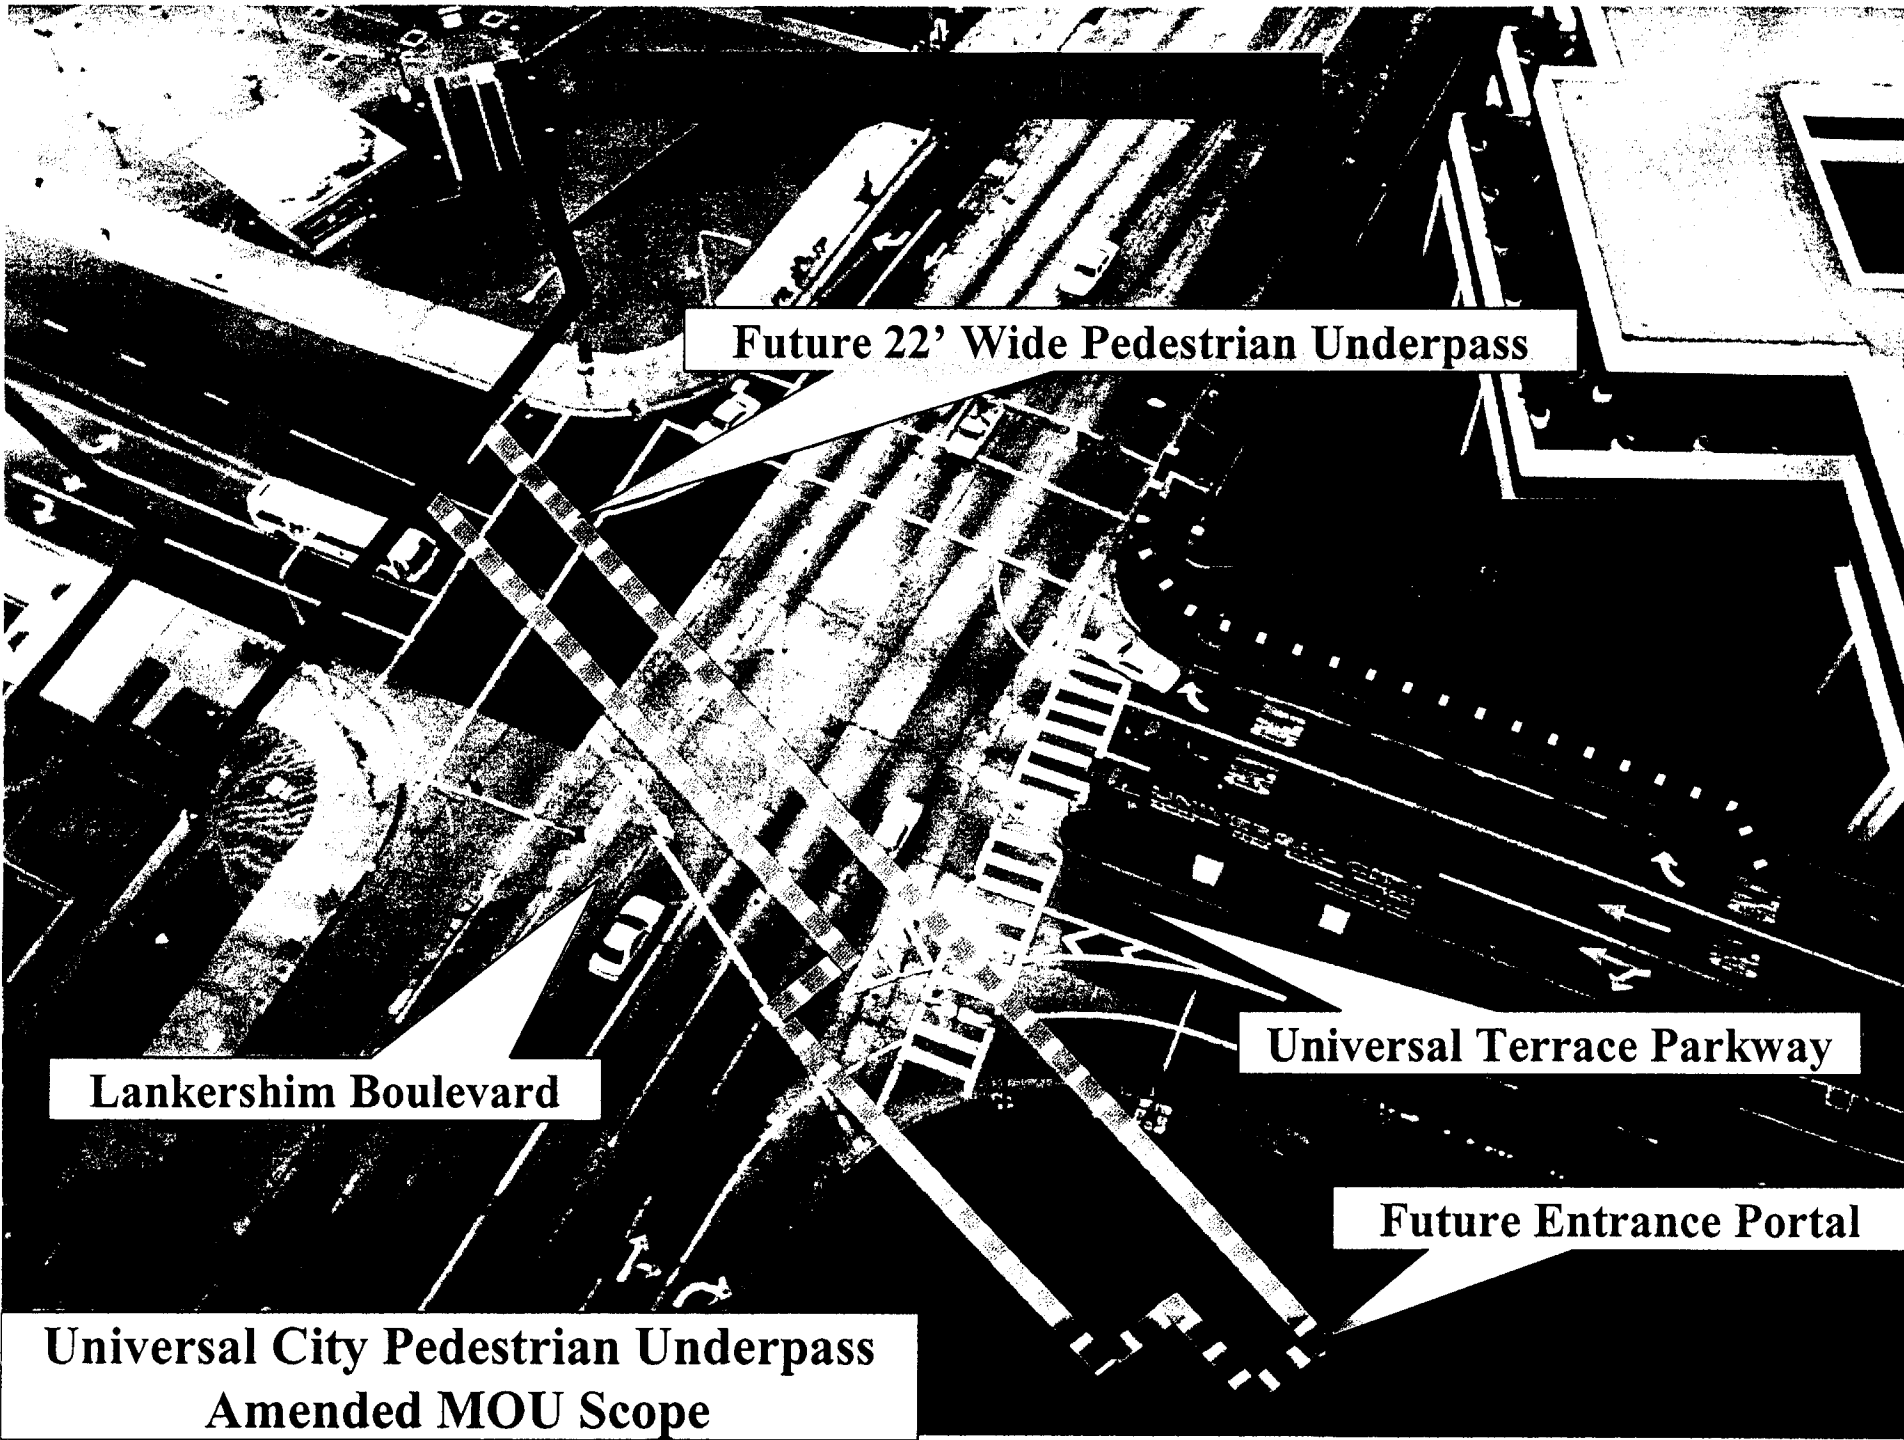

Future 22' Wide Pedestrian Underpass

Lankershim Boulevard

Universal Terrace Parkway

Future Entrance Portal

**Universal City Pedestrian Underpass
Amended MOU Scope**

Contract E0070 – EMC CW071 Pedestrian Underpass Redesign

- **EMC began redesign in June 2001 under a Limited Notice to Proceed (LNTP).**
- **MTA Board approval required for full funding of redesign.**
- **Final design scheduled to be complete by October 2001.**

